



BOWIE STREET (124' R.O.W.)

CORAL STREET (60' R.O.W.)


PROPOSED 3-STORY BUILDING  
FFE=33.45

RSONS STREET (80' R.O.W.)

DAHLIA STREET (55' R.O.W.)

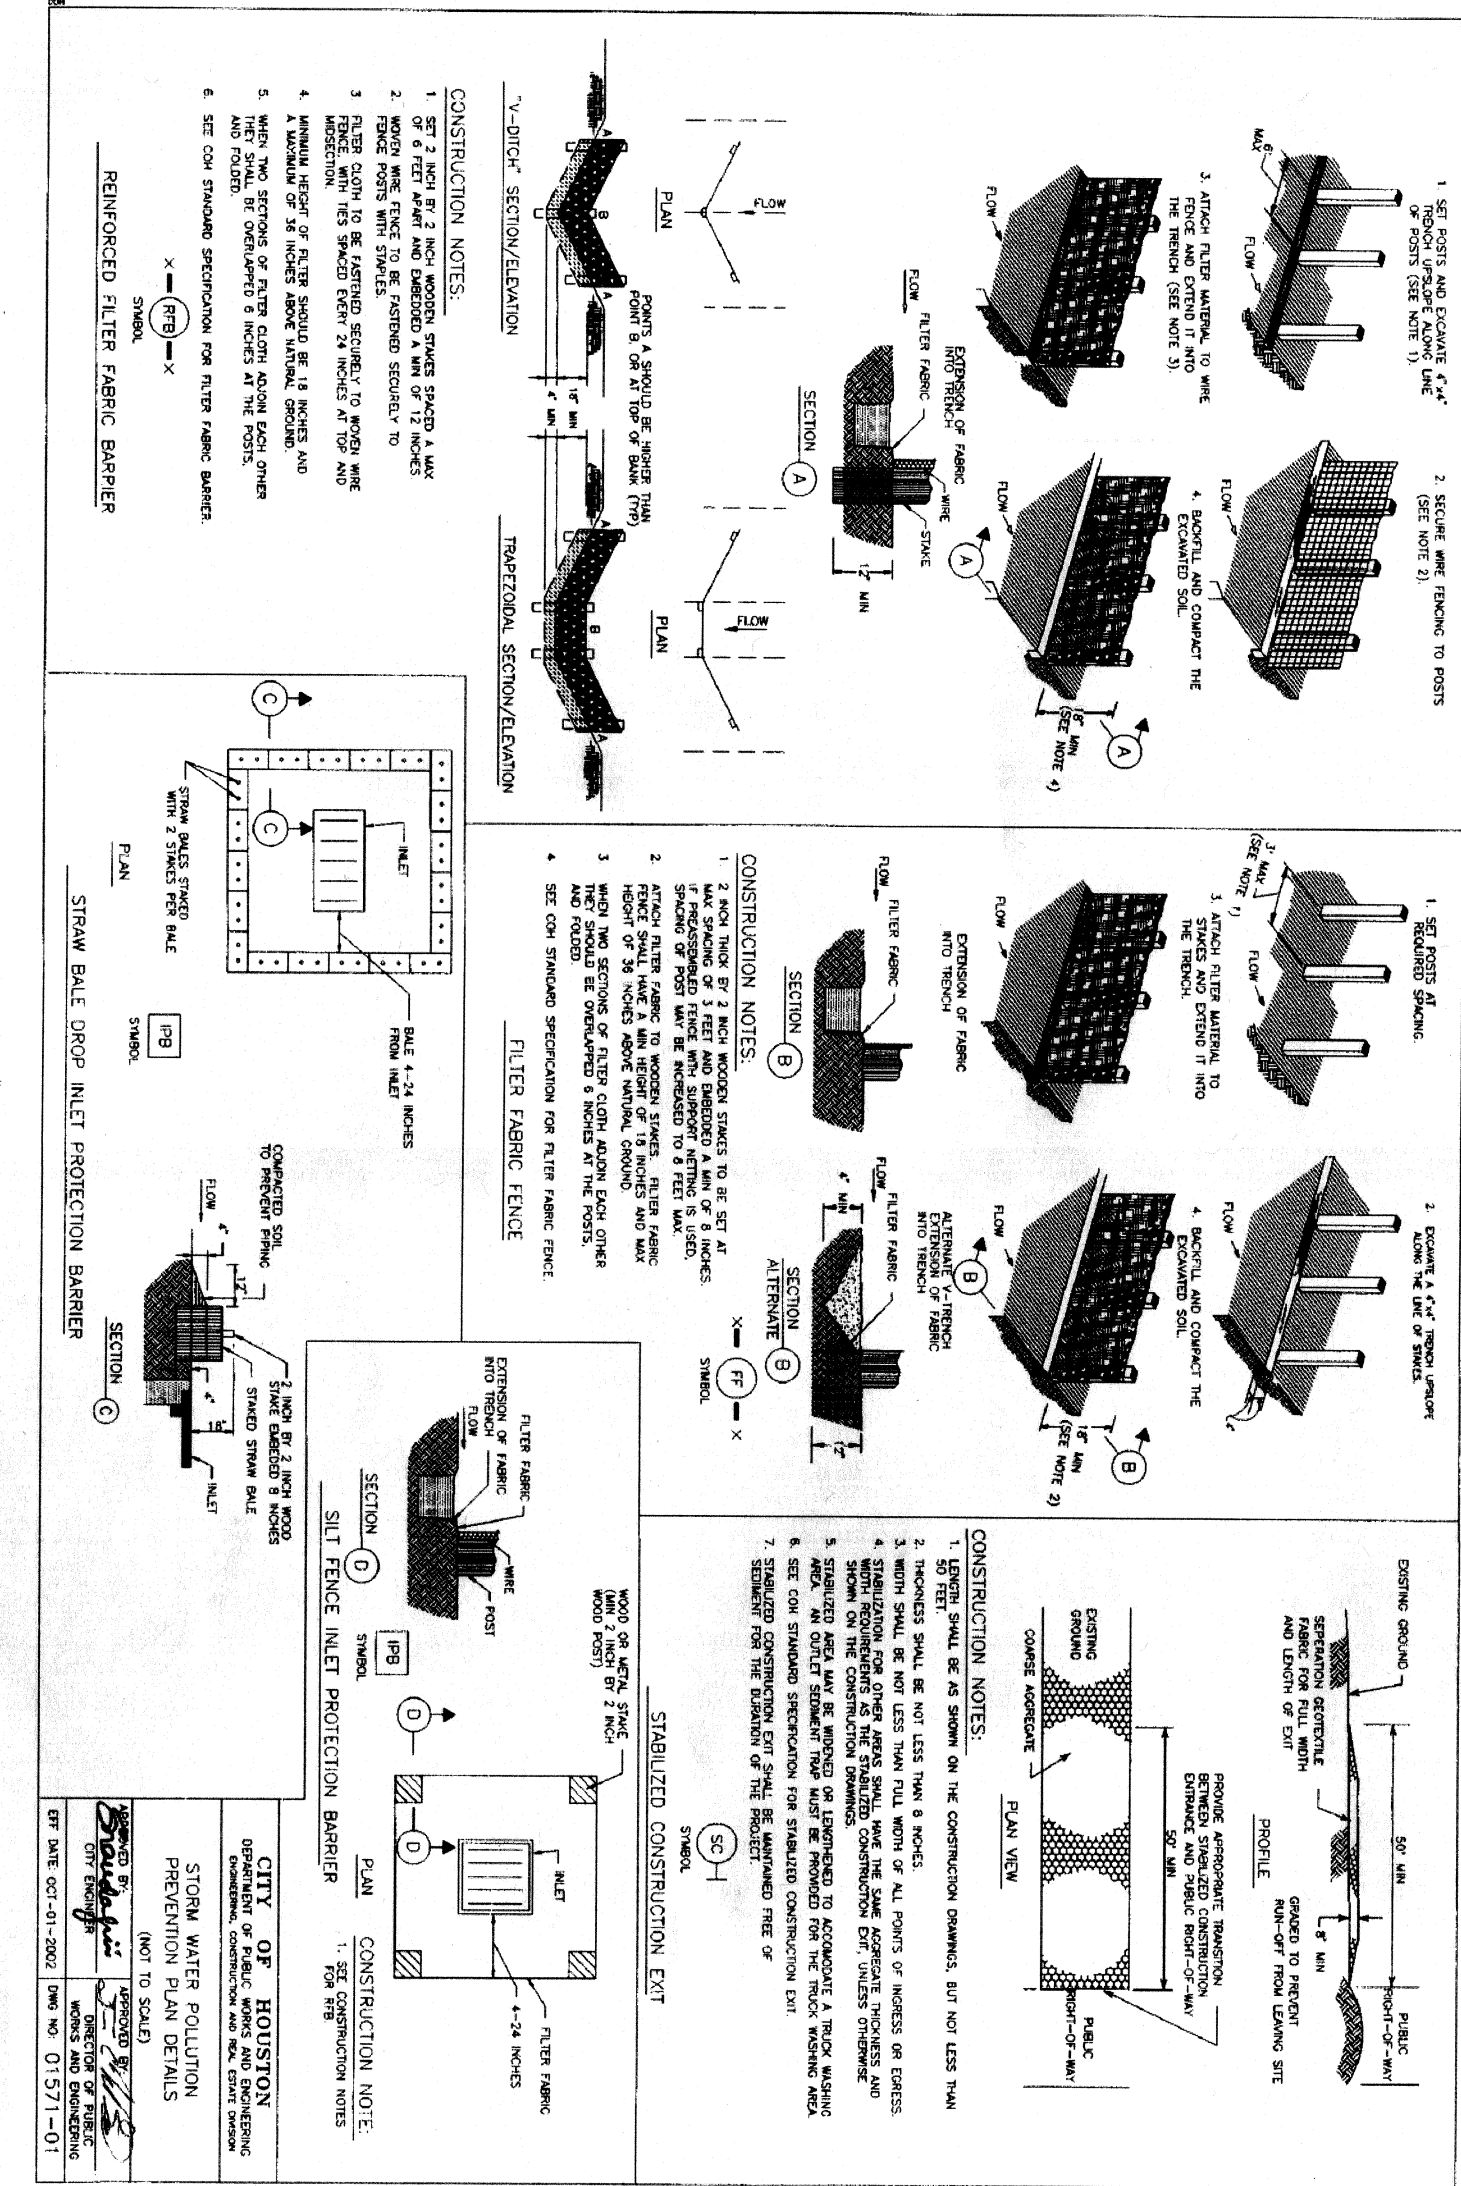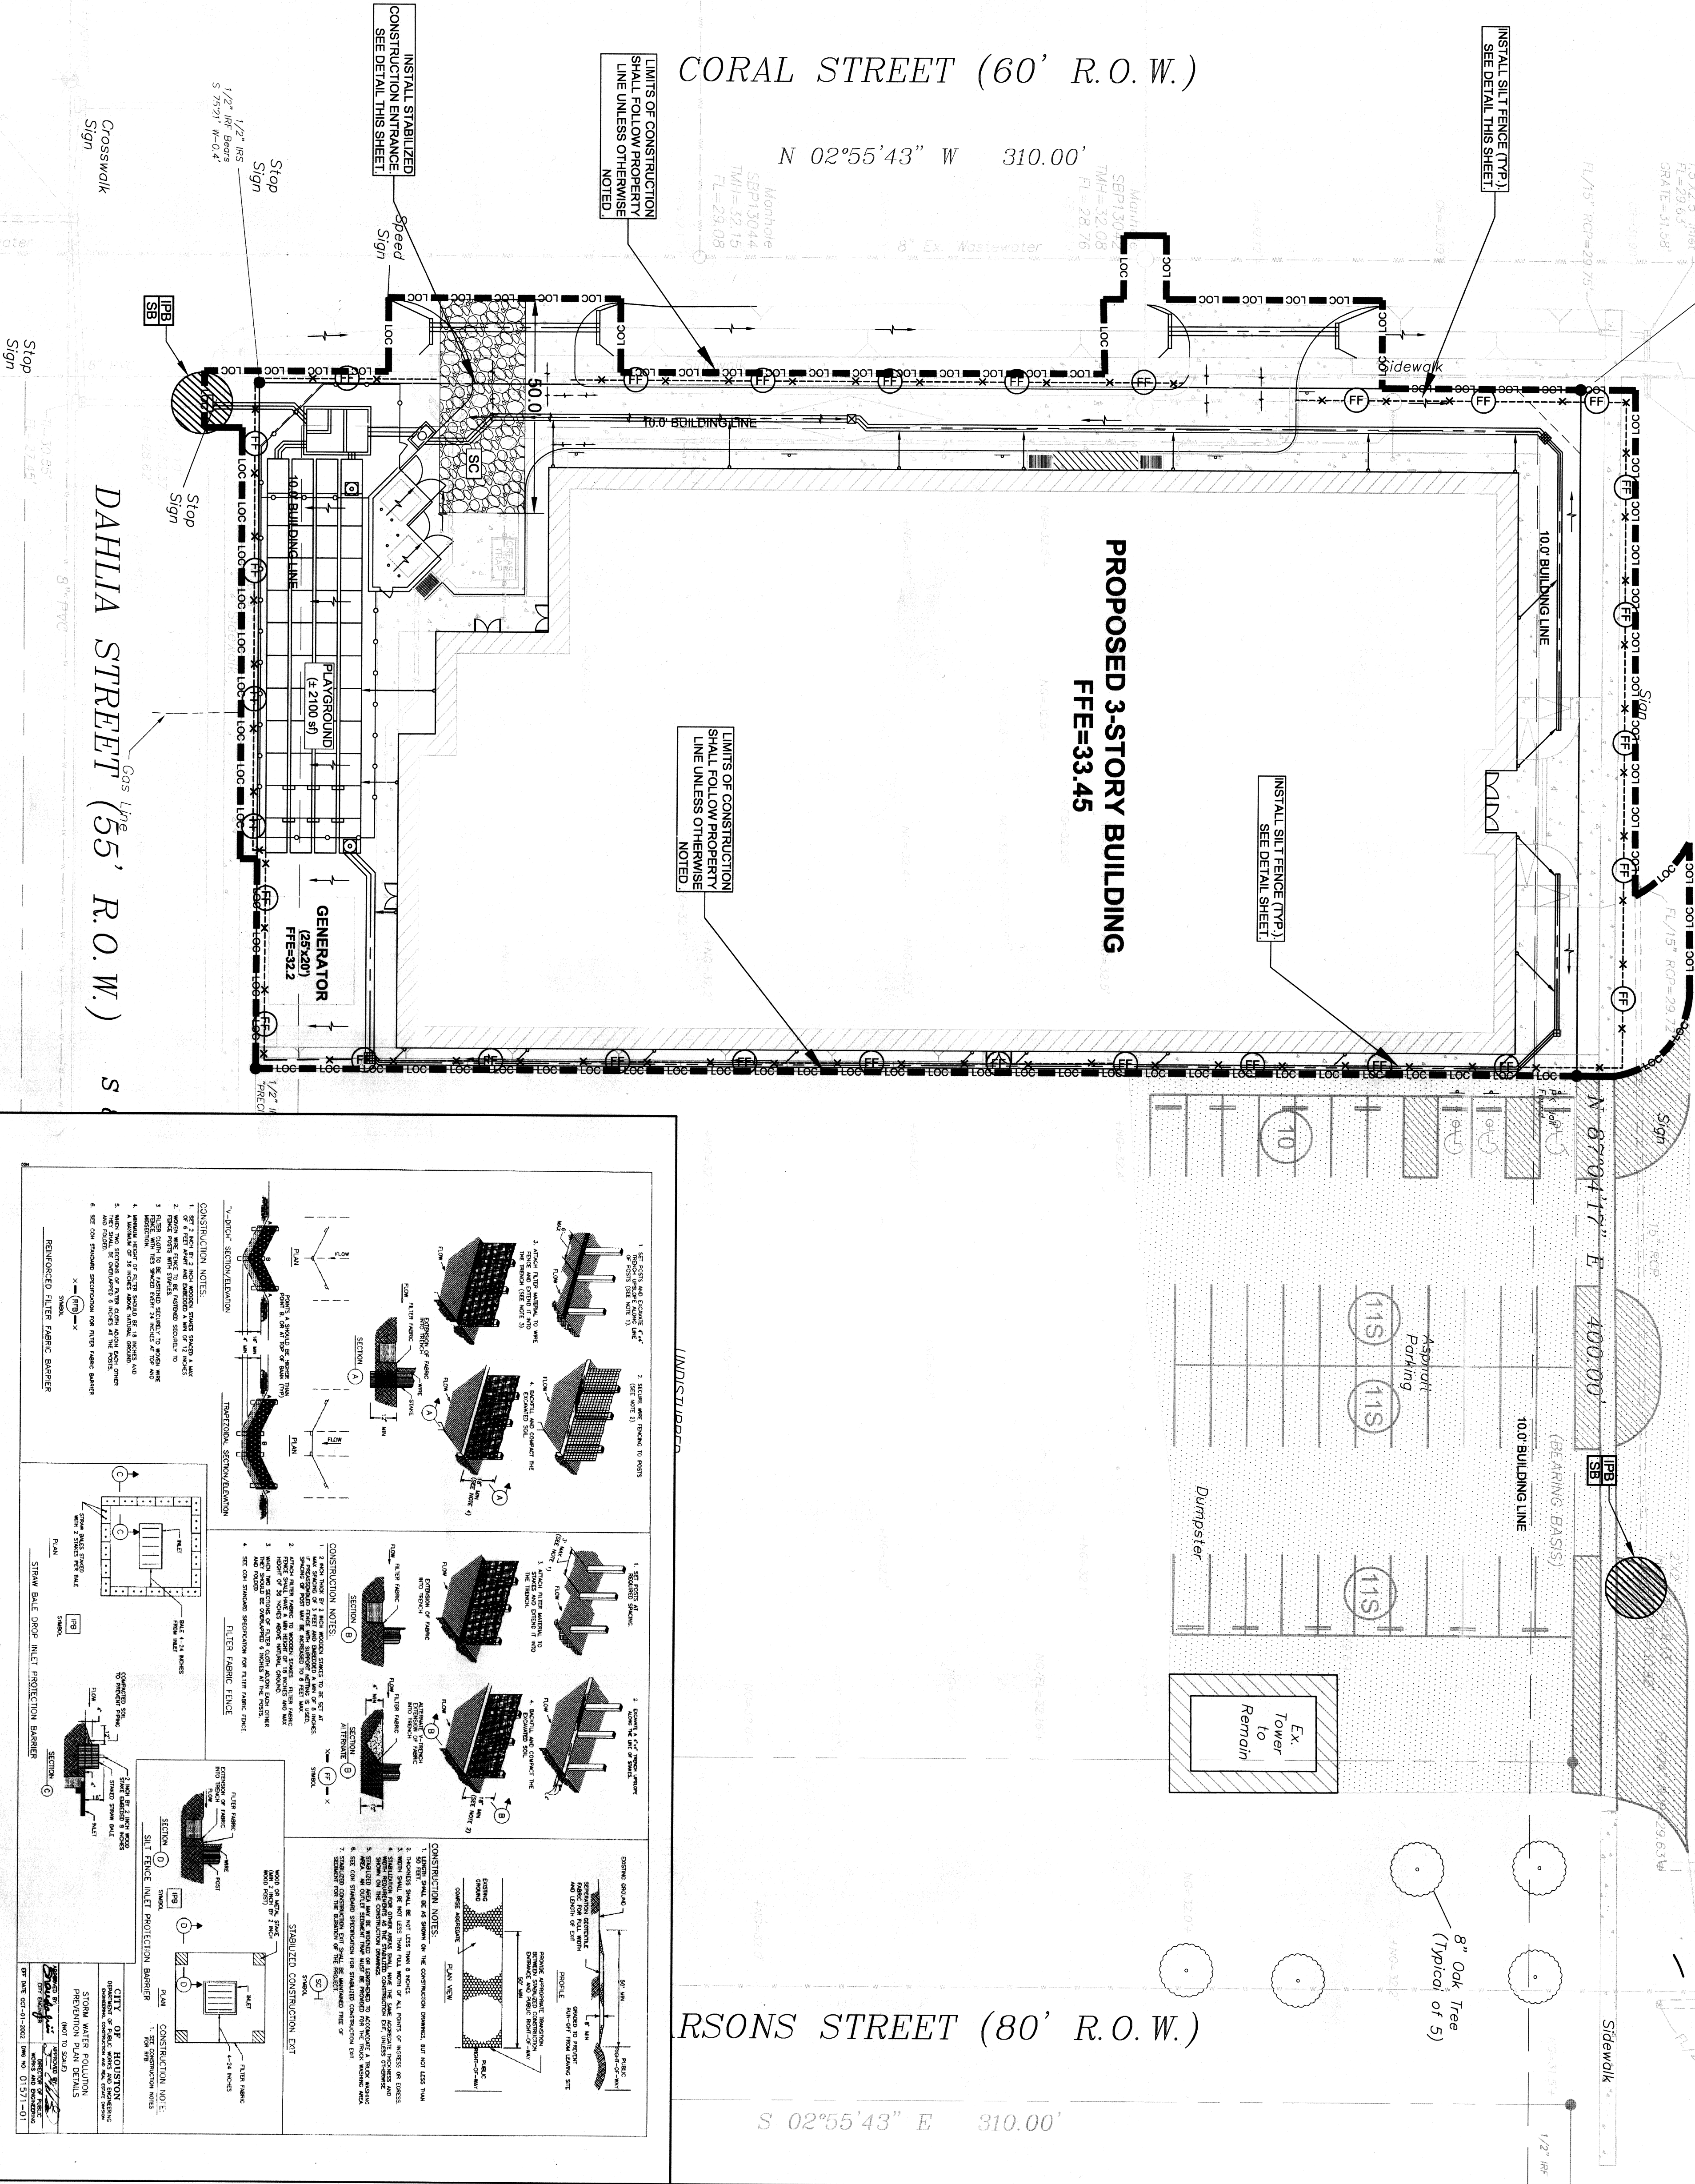

- EROSION CONTROL NOTES**
- CONTRACTOR SHALL LOCATE ALL SPOILS STORED ON SITE IN THE APPROVED TEMPORARY SPOILS LOCATION. THIS LOCATION MAY BE ADJUSTED THROUGHOUT THE COURSE OF CONSTRUCTION WITH THE APPROVAL OF THE ENVIRONMENTAL INSPECTOR. CONTRACTOR SHALL MAINTAIN SILT FENCE DOWNGRADIENT OF THE SPOILS STORAGE AREA AT ALL TIMES.
  - CONTRACTOR SHALL COMPLY WITH APPLICABLE FEDERAL ENVIRONMENTAL REGULATIONS THROUGHOUT THE COURSE OF CONSTRUCTION, INCLUDING PREPARATION & SUBMITTAL OF THE E.P.A. NOTICE OF INTENT (NOI) & STORMWATER POLLUTION PREVENTION PLAN (SWPPP) AS APPLICABLE.
  - CONTRACTOR SHALL MAINTAIN TEMPORARY EROSION CONTROLS AS PER CITY, STATE & FEDERAL GUIDELINES. CONTRACTOR SHALL REVEGETATE ALL DISTURBED AREAS. SEE RESTORATION NOTES SHEET.
  - CONTRACTOR SHALL PROVIDE APPROPRIATE DUST CONTROL MEASURES (SPRINKLES, ETC.) AS NECESSARY THROUGHOUT CONSTRUCTION.
  - CONTRACTOR SHALL AVOID TRACKING DIRT AND MUD INTO PUBLIC STREETS. DIRT AND MUD TRACKED INTO THE STREETS SHALL BE CLEANED UP IMMEDIATELY.
  - SILT FENCE IS SHOWN IN APPROXIMATE LOCATION ONLY FOR CLARITY. THE ACTUAL LOCATION OF THE SILT FENCE WILL BE AT THE LIMITS OF CONSTRUCTION WHERE APPLICABLE.
  - SILT FENCE LOCATED ON PAVEMENT SHALL BE TRIANGULAR FILTER DIKE. SEE DETAIL.

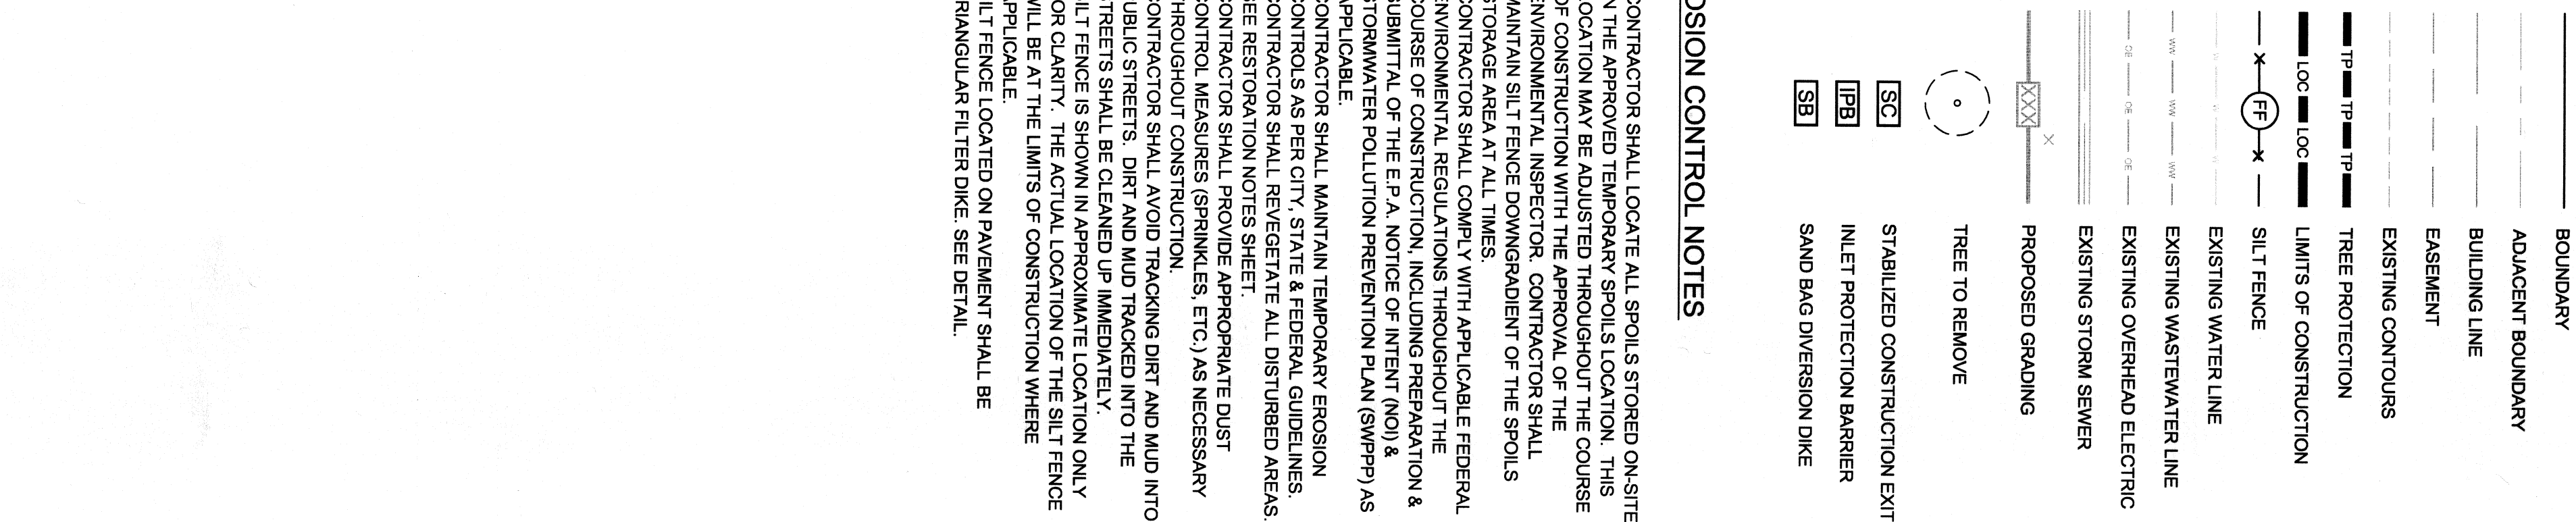

**STORMWATER POLLUTION PREVENTION PLAN**

**DATE** 10/29/09

**PROJECT #** 302-103

**CITY OF HOUSTON**

STORM WATER POLLUTION PREVENTION PLAN DETAILS

10/29/09

10/29/09

10/29/09

**BOWIE STREET CAMPUS**

7310 BOWIE STREET

HOUSTON, TX 77012

**HATCH + ULLAND OWEN ARCHITECTS**

**TEXAS DESIGN INTERESTS, LLC**

6001 W. WILLIAM CANNON

BUILDING 2, SUITE 203-C

AUSTIN, TX 78749

(512) 301-3389 (o)

(512) 301-3348 (f)

COMMERCIAL/RESIDENTIAL - CIVIL & STRUCTURAL ENGINEERING

**C4**

4 OF 16
